


## Activities of the project "Decommissioning of the Maišiagala Radioactive Waste Storage Facility"

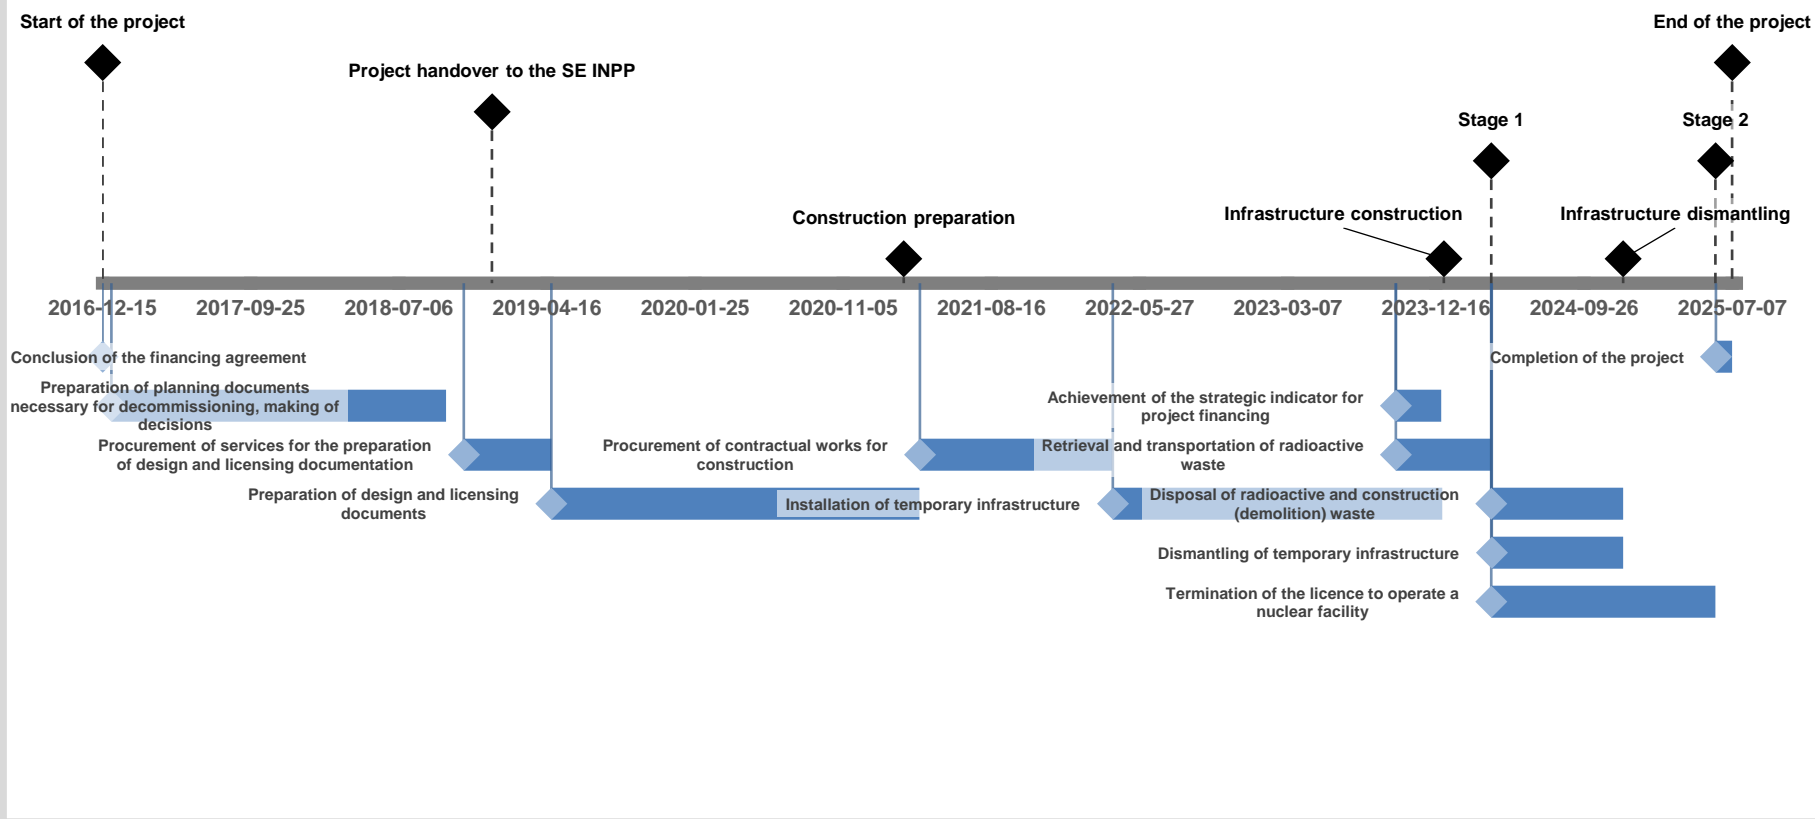

### Guidelines - Tasks

| Start      | End        | Duration | Title  | Position (p.) | Position (ž.) |
|------------|------------|----------|--|---------------|---------------|
| 2016-12-15 | 2016-12-15 | 0        | Conclusion of the financing agreement  | -15           | -15           |
| 2017-01-01 | 2018-10-05 | 642      | Preparation of planning documents necessary for decommissioning, making of decisions | -25           | -25           |

|                |            |     |   |     |     |
|----------------|------------|-----|---|-----|-----|
| 2018-11-08     | 2019-04-25 | 168 | Procurement of services for the preparation of design and licensing documentation | -35 | -35 |
| 2019-04-25     | 2021-03-31 | 706 | Preparation of design and licensing documents                                     | -45 | -45 |
| 2021-04-01     | 2022-04-05 | 369 | Procurement of contractual works for construction                                 | -35 | -35 |
| 2022-04-06     | 2023-12-29 | 632 | Installation of temporary infrastructure  | -45 | -45 |
| 2023-10-01     | 2023-12-27 | 87  | Achievement of the strategic indicator for project financing                      | -25 | -25 |
| 2023-10-01     | 2024-04-01 | 183 | Retrieval and transportation of radioactive waste                                 | -35 | -35 |
| 2024-04-01     | 2024-12-10 | 253 | Disposal of radioactive and construction (demolition) waste                       | -45 | -45 |
| 2024-04-02     | 2024-12-10 | 252 | Dismantling of temporary infrastructure   | -55 | -55 |
| 2024-04-01     | 2025-06-05 | 430 | Termination of the licence to operate a nuclear facility                          | -65 | -65 |
| 2025-06-06     | 2025-07-07 | 31  | Completion of the project   | -15 | -15 |
| <i>/terpti</i> |            |     |   |     |     |

## Stages - Substages

| Date           | Title                           | Position |
|----------------|---------------------------------|----------|
| 2016-12-15     | Start of the project            | 45       |
| 2019-01-01     | Project handover to the SE INPP | 35       |
| 2021-03-01     | Construction preparation        | 5        |
| 2024-01-01     | Infrastructure construction     | 5        |
| 2024-04-01     | Stage 1                         | 25       |
| 2024-12-10     | Infrastructure dismantling      | 5        |
| 2025-06-05     | Stage 2                         | 25       |
| 2025-07-07     | End of the project              | 45       |
| <i>/terpti</i> |                                 |          |
